

Date: Wednesday, 7/5/2006 2:40:47 PM
 User: Kim Johnston

Process Sheet

Customer : CU-DAR001 Dart Helicopters Services	Drawing Name : 350/355 AS X-TUBE FWD
Job Number : 27823	
Estimate Number : 12485	
P.O. Number : <i>N/A</i>	Part Number : D350748101
This Issue : 7/5/2006 S.O. No. : <i>N/A</i>	Drawing Number : IIN D350-748 P5 PREL <i>06.07.05</i>
Prsht Rev. : NC	Project Number : N/A
First Issue : <i>N/A</i>	Drawing Revision : PREL
Previous Run : <i>N/A</i>	Material : <i>N/A</i>
Written By : <i>[Signature]</i>	Due Date : 7/30/2006 Qty: 1 Um: Each
Checked & Approved By : <i>[Signature] 06.07.05</i>	
Comment : Est Rev A New Issue 06-07-05 JLM	

Additional Product

Job Number:



Seq. #:	Machine Or Operation:	Description :
---------	-----------------------	---------------

1.0	DC	DOCUMENT CONTROL
-----	----	------------------



①

Comment: Photocopy bluefile & type labels per PPPD350-748-101	CHG001
---	--------

06-07-29 KT

2.0	27823A	X-TUBE AS 350/355 HI FWD
-----	--------	--------------------------



Comment: Sub-Component X-TUBE AS 350/355 HI FWD

3.0	PACKAGING 1	PACKAGING RESOURCE #1
-----	-------------	-----------------------



Comment: PACKAGING RESOURCE #1
Pick Packing Kit

4.0	D35001	350 SADDLE
-----	--------	------------



Comment: Qty.: 4.0000 Each(s)/Unit Total : 4.0000 Each(s)
350 SADDLE
Batch: <i>228096</i> <i>B28096</i> ✓

5.0	D35011	BUSHING
-----	--------	---------



Comment: Qty.: 16.0000 Each(s)/Unit Total : 16.0000 Each(s)
BUSHING
Batch: <i>1128127</i>

6.0	AN46A	Bolt
-----	-------	------



Comment: Qty.: 16.0000 Each(s)/Unit Total : 16.0000 Each(s)
Bolt
Batch: <i>1101418</i> ✓

06/09/08

W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Mfg / Design Mgr	Approval QC Inspector

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Design Mgr	Approval QC Inspector
			Initial Design Mgr	Action Description Design Mgr	Sign & Date			

Part No: _____ PAR #: _____ Fault Category: _____ NCR: Yes No DQA: _____ Date: _____

NOTE: Date & initial all entries

QA: N/C Closed: _____ Date: _____

Date: Wednesday, 7/5/2006 2:40:47 PM
User: Kim Johnston

Process Sheet

Customer: CU-DAR001 Dart Helicopters Services

Drawing Name: 350/355 AS X-TUBE FWD

Job Number: 27823

Part Number: D350748101

Job Number:



Seq. #:

Machine Or Operation:

Description :

7.0

AN441A

bolt



Comment: Qty.: 8.0000 Each(s)/Unit Total: 8.0000 Each(s)

bolt

Batch: M101538 ✓

8.0

AN532A

Bolt



Comment: Qty.: 4.0000 Each(s)/Unit Total: 4.0000 Each(s)

Bolt

Batch: M101648 ✓

9.0

AN960JD416

Washer



Comment: Qty.: 32.0000 Each(s)/Unit Total: 32.0000 Each(s)

Washer

Batch: M19185 ✓

10.0

AN960JD516

Washer



Comment: Qty.: 8.0000 Each(s)/Unit Total: 8.0000 Each(s)

Washer

Batch: M101369 ✓

11.0

MS21042L4

Nut



Comment: Qty.: 24.0000 Each(s)/Unit Total: 24.0000 Each(s)

Nut

Batch: M19099 ✓

12.0

MS21042L5

Nut



Comment: Qty.: 1.0000 Each(s)/Unit Total: 1.0000 Each(s)

Nut

Batch: M101648 ✓

2506/09/28

13.0

QC4

INSPECT 100% KITS FOR COMPLETENESS



Comment: INSPECT 100% KITS FOR COMPLETENESS

104/29 (1)

W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Mfg / Design Mgr	Approval QC Inspector

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Design Mgr	Approval QC Inspector
			Initial Design Mgr	Action Description Design Mgr	Sign & Date			

Part No: _____ PAR #: _____ Fault Category: _____ NCR: Yes ☐ No ☒ DQA: ☒ Date: 06/05/29

NOTE: Date & initial all entries

QA: N/C Closed: _____ Date: _____

Date: Wednesday, 7/5/2006 2:40:47 PM
User: Kim Johnston

Process Sheet

Customer: CU-DAR001 Dart Helicopters Services

Drawing Name: 350/355 AS X-TUBE FWD

Job Number: 27823

Part Number: D350748101

Job Number:



Seq. #:

Machine Or Operation:

Description :

14.0

PACKAGING 1

PACKAGING RESOURCE #1



Comment: PACKAGING RESOURCE #1

Identify and pack for shipping as per PPP D350-748-101

Location:

PPP Rev:

OPR PA

Rec'd 7/29

[Signature]

15.0

DC

DOCUMENT CONTROL



Comment: DOCUMENT CONTROL

Inspection Level 21

[Signature] ①
06/09/29

Job Completion



W 06-09-29

W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Mfg / Design Mgr	Approval QC Inspector

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Design Mgr	Approval QC Inspector
			Initial Design Mgr	Action Description Design Mgr	Sign & Date			

Part No: _____ PAR #: _____ Fault Category: _____ NCR: Yes No DQA: _____ Date: _____

NOTE: Date & initial all entries

QA: N/C Closed: _____ Date: _____

3.10 Apply a continuous bead of Sikaflex-241/-291 or Proseal 890 or MIL-S-8802 Class B2 sealant in the following locations as per Figure 6:

- A) Along saddle/crosstube interface.
- B) Between the saddle flanges.
- C) Along saddle/skidtube interface.

4.0 WEIGHT AND BALANCE

The following weight and balance information is for Dart crosstube installations only. This data should be similar to the existing installation. Differences from the parts removed are the responsibility of the installer.

DART CROSSTUBE	FWD/AFT	WEIGHT	STA	MOMENT
D350-748-101	Fwd	35.2 lb (16.0 kg)	106.3 in (2.70 m)	3742 lb-in (43.2 kg-m)
D350-748-201	Aft	34.7 lb (15.7 kg)	162.4 in (4.12 m)	5635 lb-in (64.7 kg-m)

5.0 PARTS LIST

Qty -101	Qty -201	Part Number	Description
X		D350-748-101	CROSSTUBE INSTALLATION, AS 350/355 HIGH FWD
	X	D350-748-201	CROSSTUBE INSTALLATION, AS 350/355 HIGH AFT
1		D350-748-141	CROSSTUBE ASSEMBLY, AS 350/355 HIGH FWD
	1	D350-748-241	CROSSTUBE ASSEMBLY, AS 350/355 HIGH AFT
*2	*2	D3502-1	SUPPORT
*2	*2	D2856-400-710	ABRASION STRIP
*1	*1	AELS-1032-225	INSERT
*2	*2	MS21920-20	CLAMP
*1	*1	MS27039-1-10	SCREW
*1	*1	AN960JD10	WASHER
4	4	D3500-1	SADDLE
16	16	D3501-1	BUSHING
16	16	AN4-6A	BOLT
8	8	AN4-41A	BOLT
4	4	AN5-32A	BOLT
32	32	AN960JD416	WASHER
8	8	AN960JD516	WASHER
24	24	MS21042L4	NUT (OR MS21042-4)
4	4	MS21042L5	NUT (OR MS21042-5)

* REFERENCE ONLY. PARTS ARE INCLUDED IN D350-748-141/241 ASSEMBLIES ABOVE

SHOP COPY
RETURN TO
ENGINEERING
UNCONTROLLED COPY
SUBJECT TO AMENDMENT
WITHOUT NOTICE
WORK ORDER
NO. 27823

Date: Wednesday, 7/5/2006 2:41:02 PM
 User: Kim Johnston

Process Sheet

Customer : CU-DAR001 Dart Helicopters Services Drawing Name : X-TUBE AS 350/355 HI FWD
 Job Number : 27823A
 Estimate Number : 12484
 P.O. Number : N/A Part Number : D350748141
 This Issue : 7/5/2006 S.O. No. : N/A Drawing Number : D350-748-141 PREL
 Prsht Rev. : NC Project Number : N/A
 First Issue : N/A Type : LANDING GEAR Drawing Revision : PREL
 Previous Run : N/A Material : N/A
 Written By : Due Date : 7/30/2006 Qty: 1 Um: Each
 Checked & Approved By : *06-07-05*
 Comment : Est Rev: A New Issue 06-07-05 JLM

Additional Product

Job Number:



Seq. #: Machine Or Operation: Description :

1.0 DC DOCUMENT CONTROL



Comment: DOCUMENT CONTROL

Photocopy bluefile and create labels as per PPP D350-748-141 CHG001

06-09-09

2.0 D6017115 Crosstube Material



Comment: Qty.: 1.0000 Each(s)/Unit Total: 1.0000 Each(s)

Crosstube Material

D6017-115

2.339" OD X 2.000" ID

Batch: *B27318**10069**ml 06/07/14*

3.0 MORI SEIKI MORI SEIKI CNC LATHE LARGE



Comment: MORI SEIKI CNC LATHE LARGE

1-Fill tube with sand & install plugs DT *NA* on both ends as per Folio FA648

2-Turn first side as per Folio FA648

ml 06/07/14

3-Deburr & Inspect for surface damage. Repair damage within limits as per Dwg D350-748-141.

4.0 QC1 INSPECT ALL DIM TO DIM SHEET



Comment: INSPECT ALL DIM TO DIM SHEET

ml 06/07/14

W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Mfg / Design Mgr	Approval QC Inspector
06/10/03	14	CAD Plate and Magnetic Particle Inspect per D350-742-141 Rev L Acceptable to CAD Plate to spec AMS-QQ-P-416B See attached DS email				CP 06.10.03 Pw QSI 042	

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Design Mgr	Approval QC Inspector
			Initial Design Mgr	Action Description Design Mgr	Sign & Date			

Part No: _____ PAR #: _____ Fault Category: _____ NCR: Yes No DQA: _____ Date: _____

NOTE: Date & initial all entries

QA: N/C Closed: _____ Date: _____

Date: Wednesday, 7/5/2006 2:41:02 PM
User: Kim Johnston

Process Sheet

Customer: CU-DAR001 Dart Helicopters Services

Drawing Name: X-TUBE AS 350/355 HI FWD

Job Number: 27823A

Part Number: D350748141

Job Number:



Seq. #: Machine Or Operation: Description :

5.0 MORI SEIKI MORI SEIKI CNC LATHE LARGE



Comment: MORI SEIKI CNC LATHE LARGE

1-Turn second side as per Folio FA648

2-Deburr & Inspect for surface damage. Repair damage within limits as per Dwg D350-748-141. *BC 06.07.15*

6.0 QC1 INSPECT ALL DIM TO DIM SHEET



Comment: INSPECT ALL DIM TO DIM SHEET

7.0 QC8 SECOND CHECK



Comment: SECOND CHECK

8.0 OUTSIDE SERVICE OUTSIDE SERVICES



Comment: Sub-Contracting OUTSIDE SERVICES

Issue P/O: *1708*

Heat Treat to min 180 KSI As per Dwg D350-748-141 *U*

Sand Blast tube after Heat Treat

Possible Supplier: Vac Aero

Ensure Certificate of Conformity is attached

06-07-18

SEE ATTACHED Deviation

9.0 PACKAGING 1 PACKAGING RESOURCE #1



Comment: PACKAGING RESOURCE #1

Receive & Inspect For Transit Damage

Ensure certificate of conformaty is attached *LS 06/07/13*

10.0 QC6 DIMENSIONAL CHECK



Comment: DIMENSIONAL CHECK *AB 06-09-14*

11.0 BENDING BENDING MACHINE



Comment: BENDING MACHINE

Bend tube as per Dwg D350-748-141 using CNC bender program _____ and Folio FT _____ *06-08-04*

QC6 dim. check.

06-07-10 *(P10)*

POSITIVE
RECALL

W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Mfg / Design Mgr	Approval QC Inspector
060809	11.1	QC 6 dim check before drilling perm change.					<i>[Signature]</i> 060809

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Design Mgr	Approval QC Inspector
			Initial Design Mgr	Action Description Design Mgr	Sign & Date			

Part No: _____ PAR #: _____ Fault Category: _____ NCR: Yes No DQA: _____ Date: _____

NOTE: Date & initial all entries

QA: N/C Closed: _____ Date: _____

Date: Wednesday, 7/5/2006 2:41:03 PM
User: Kim Johnston

Process Sheet

Customer: CU-DAR001 Dart Helicopters Services

Drawing Name: X-TUBE AS 350/355 HI FWD

Job Number: 27823A

Part Number: D350748141

Job Number:



Seq. #:	Machine Or Operation:	Description :
---------	-----------------------	---------------

12.0	LANDING GEAR 1	LANDING GEAR RESOURCE 1
------	----------------	-------------------------



Comment: LANDING GEAR RESOURCE 1

1-Remove all marks from tube within limits of D350-748-141

2-Drill Tube as per Dwg D350-748-141

3-Deburr

4-Engrave Part # and Batch # as per Dwg D350-748-141

Pin 06-08-140

DP 6-8-25

Done at Seq # 5

13.0	DIMENSIONAL CHECK	
------	-------------------	--

QLS



Comment: DIMENSIONAL CHECK

Done at Seq # 11

06-09-07
06-09-07

14.0	OUTSIDE SERVICE	OUTSIDE SERVICES
------	-----------------	------------------



Comment: Sub-Contracting OUTSIDE SERVICES

Liquid Penetrant Inspection as per QSI 038

Issue P/O: *2000*

LPI as per ASTM 1417 Level 2

Attach copy of NDT results to work order

C 06/09/11

See Attached Deviation

15.0	PACKAGING 1	PACKAGING RESOURCE #1
------	-------------	-----------------------



Comment: PACKAGING RESOURCE #1

Inspect for transit damage Ensure copy of NDT results attached to work order.

W 06/09/11

16.0	DIMENSIONAL CHECK	
------	-------------------	--



Comment: Inspect for damage & ensure results are as per Dwg D350-748-241

06-09-28

17.0	SPRAY PAINTING	SPRAY PAINTING
------	----------------	----------------



Comment: SPRAY PAINTING

1-Prime inside crosstube as per QSI 005 4.2

PRIME OUTSIDE OF CROSSTUBE PER QSI 005 4.2

06-09-28

06-09-25

W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Mfg / Design Mgr	Approval QC Inspector
06.09.25	17 19	PRIME INSIDE & OUTSIDE OF TUBE THEN PAINT PER Q5160542 PER DWG D350-748-141 Rev C	MM	06.09.28	1	CP 06.09.25 per Q51642	

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Design Mgr	Approval QC Inspector
			Initial Design Mgr	Action Description Design Mgr	Sign & Date			

Part No: _____ PAR #: _____ Fault Category: _____ NCR: Yes No DQA: _____ Date: _____

NOTE: Date & initial all entries

QA: N/C Closed: _____ Date: _____

Date: Wednesday, 7/5/2006 2:41:03 PM
User: Kim Johnston

Process Sheet

Customer: CU-DAR001 Dart Helicopters Services

Drawing Name: X-TUBE AS 350/355 HI FWD

Job Number: 27823A

Part Number: D350748141

Job Number:



Seq. #:

Machine Or Operation:

Description :

18.0

QC14

Inspect Spray Paint



Comment: Inspect Spray Paint

Then, Wrap in plastic bag to protect from scratches

N/A

19.0

POWDER COATING

PAINT

POWDER COATING



Comment: POWDER COATING

PAINT OUTSIDE OF CRUSSTUBE PER PART QSI 605 4.2

Powder Coat White Gloss (Ref: 4.3.5.4) as per QSI 005 4.3

0609.25

ML 03 03 28

①

20.0

QC14

INSPECT POWDER COAT/CHEMICAL CONVERSION



Comment: INSPECT POWDER COAT/CHEMICAL CONVERSION

PAINT

0609-29 ①

21.0

D35021

SUPPORT



Comment: Qty.: 2.0000 Each(s)/Unit Total: 2.0000 Each(s)

SUPPORT

Batch: 27874

0609.25

22.0

D2856400

Abrasion Strip



Comment: Qty.: 1.2401 f(s)/Unit Total: 1.2401 f(s)

Abrasion Strip 7.10" long x2

Batch: 27545

23.0

ALS41032225

Insert



Comment: Qty.: 1.0000 Each(s)/Unit Total: 1.0000 Each(s)

Insert

Batch: 100489

24.0

AN960JD10

Washer



Comment: Qty.: 1.0000 Each(s)/Unit Total: 1.0000 Each(s)

Washer

Batch: 100713

W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Mfg / Design Mgr	Approval QC Inspector

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Design Mgr	Approval QC Inspector
			Initial Design Mgr	Action Description Design Mgr	Sign & Date			

Part No: _____ PAR #: _____ Fault Category: _____ NCR: Yes ☒ No ☐ DQA: ☒ Date: 06/10/03

NOTE: Date & initial all entries

QA: N/C Closed: _____ Date: _____

Date: Wednesday, 7/5/2006 2:41:03 PM
User: Kim Johnston

Process Sheet

Customer: CU-DAR001 Dart Helicopters Services

Drawing Name: X-TUBE AS 350/355 HI FWD

Job Number: 27823A

Part Number: D350748141

Job Number:



Seq. #:

Machine Or Operation:

Description :

25.0

MS2192020

Clamp (per MIL-DTL-8783C)



X Comment: Qty.: 2.0000 Each(s)/Unit Total: 2.0000 Each(s)
Clamp (per MIL-DTL-8783C)
Batch: M15936

26.0

~~MS35206344~~

MS27039-1-10

Screw



X Comment: Qty.: 1.0000 Each(s)/Unit Total: 1.0000 Each(s)
Screw
Batch: 18836

27.0

LANDING GEAR 1

LANDING GEAR RESOURCE 1



Comment: LANDING GEAR RESOURCE 1

1-Install Ground wire Insert, then insert screw and washer

2-Install Abrasion strips as per Dwg D350-748-141 & QSI 035.

3-Install supports as per Dwg D350-748-141, Torque to 60-80 IN-LBS

DP 6-9-29

28.0

QC5

INSPECT WORK TO CURRENT STEP



Comment: INSPECT WORK TO CURRENT STEP

29.0

PACKAGING 1

PACKAGING RESOURCE #1



Comment: PACKAGING RESOURCE #1

Identify and pack for shipping as per PPP D350-748-241

Location: _____

PPP Rev: _____

Mo 6/29/29

30.0

DC

DOCUMENT CONTROL



Comment: DOCUMENT CONTROL
Inspection Level 21

06/09/29

Job Completion



POSITIVE RECALL

EFFECTIVE *06/09/29* AUTH *[Signature]*

RELEASED *[Signature]* DATE *06/09/29*

Verification cards

Verification tube dims

W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Mfg / Design Mgr	Approval QC Inspector

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Design Mgr	Approval QC Inspector
			Initial Design Mgr	Action Description Design Mgr	Sign & Date			

Part No: _____ PAR #: _____ Fault Category: _____ NCR: Yes No DQA: _____ Date: _____

NOTE: Date & initial all entries

QA: N/C Closed: _____ Date: _____

PRELIMINARY ISSUE

DESIGN 90	DRAWN BY	DART AEROSPACE LTD HAWKESBURY, ONTARIO, CANADA	
CHECKED	APPROVED	DRAWING NO. D350-748-141	REV. B SHEET 1 OF 3
DATE 06.06.30		TITLE CROSSTUBE (AS 350/355 HI FWD)	SCALE NTS
A	06.03.31	NEW ISSUE	
B	06.06.30	ADD D6017-115 & PRIME AND PAINT	

QTY	P/N	DESCRIPTION
X	D350-748-141	CROSSTUBE ASSEMBLY (AS 350/355 HI FWD)
1	D6017-115	CROSSTUBE (OR D6015-125)
2	D3502-1	SUPPORT
2	D2856-400-710	ABRASION STRIP
1	AELS-1032-225	INSERT
1	AN960JD10	WASHER
2	MS21920-20	CLAMP
1	MS35206-344	SCREW

D350-748-141 CROSSTUBE:


- MATERIAL: MANUFACTURED FROM D6017-115 OR D6015-125
FINISHED LENGTH = 110.27±0.06
- MACHINE PER MACHINING DETAIL ON PAGE 3. BLEND OUT ALL EDGES FROM MACHINING LONGITUDINALLY, TRANSITIONS SHOULD BE SMOOTH. NOTE: ALL HOLES ARE DRILLED AFTER BENDING.
- SCRIBE DART PART NUMBER AND BATCH NUMBER IN THIS AREA WITH VIBRATING STYLUS.
- BEND PROGRESSIVELY WITH A MINIMUM OF 7 PASSES. MAXIMUM TUBE FLATTENING DUE TO BENDING IS 6% BASED ON O.D.
- HEAT TREAT TO MIN. 180 KSI PER MIL-T-6736 AFTER TURNING
- LIQUID PENETRANT INSPECT OUTSIDE SURFACE OF CROSSTUBE PER QSI 038.
- FINISH: POWDER COAT WHITE (4.3.5.2) OUTSIDE PER DART QSI 005 4.3.
PRIME INSIDE PER DART QSI 005 4.2.
OR
PRIME INSIDE AND OUTSIDE PER DART QSI 005 4.2
PAINT OUTSIDE PER DART QSI 005 4.2
- EXTREME CARE MUST BE TAKEN TO PROTECT THE OUTSIDE SURFACE OF THE TUBE. THE OUTSIDE SURFACE MUST BE SMOOTH AND FREE FROM SURFACE DEFECTS SUCH AS SCRATCHES, NICKS, OR DENTS. DEFECTS UP TO 0.005" MAY BE BLENDED OUT LONGITUDINALLY. CIRCUMFERENTIAL GRIND MARKS ARE UNACCEPTABLE. WHEN DRILLING HOLES EXTREME CARE MUST BE TAKEN AND CAREFUL DEBURRING PERFORMED TO ENSURE A CLEAN HOLE WITH NO CRACKING/CHIPPING/GROOVES.
- INSTALL D2856-400-710 ABRASION STRIP WITH A GAP ON BOTTOM SIDE OF CROSSTUBE, CENTERED OPPOSITE D3502-1 SUPPORT, PER QSI 035.
- TORQUE MS21920-20 CLAMPS 60 TO 80 IN-LB
- TOLERANCES ARE PER DART QSI 018 UNLESS OTHERWISE NOTED.
- ALL DIMENSIONS ARE IN INCHES
- PART IS SYMMETRIC ABOUT CENTERLINE EXCEPT FOR Ø0.297 HOLE.

UNCONTROLLED COPY
ENGINEERING
SUBJECT TO AMENDMENT
WITHOUT NOTICE
WORK ORDER
NO. 27823A

Copyright © 2006 by DART AEROSPACE LTD


THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.

PRELIMINARY ISSUE

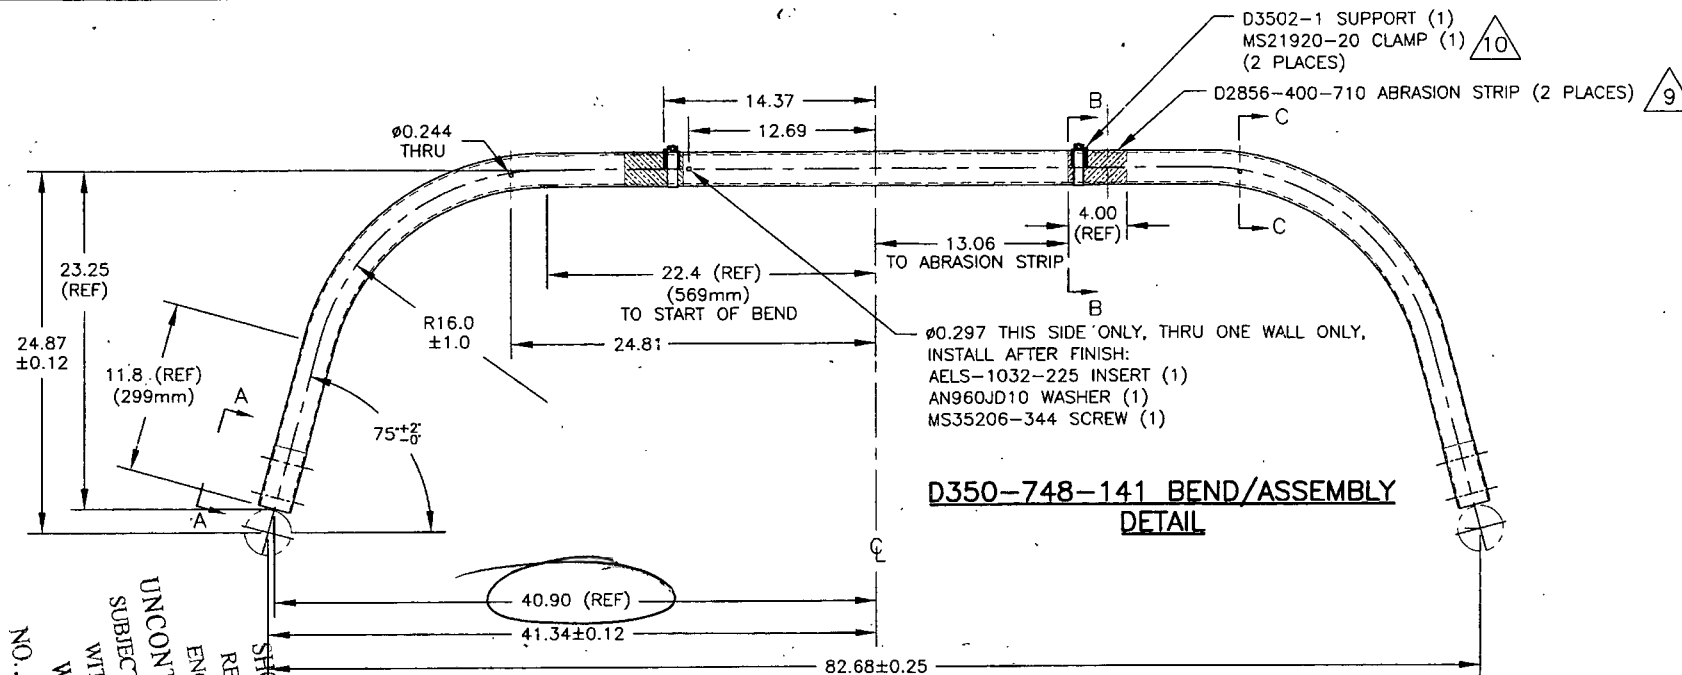


**D350-748-141 BEND/ASSEMBLY
DETAIL**


NO. 27823A
WORK ORDER
WITHOUT NOTICE
UNCONTROLLED COPY
ENGINEERING
RETURN TO
SHOP COPY

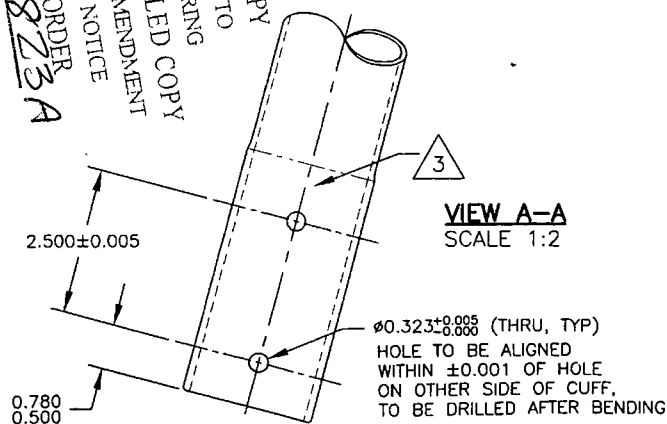


**SECTION B-B
SCALE 1:2**

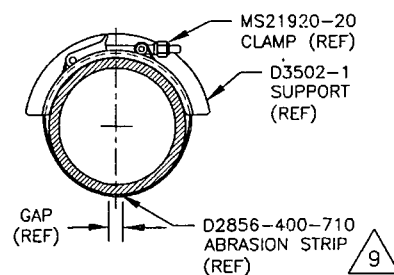


**SECTION C-C
SCALE 1:2**





COPYRIGHT © 2006 BY DART AEROSPACE LTD. THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.	DESIGN	DRAWN BY		DART AEROSPACE LTD. HAMPSHIRE, ONTARIO, CANADA
	CHECKED	APPROVED	DRAWING NO.	REV.
	DATE	TITLE	SHEET 2 OF 3	
			SCALE	

42		D350-748-141	
06.06.30	CROSSTUBE (AS 350/355 HI FWD)		1:8

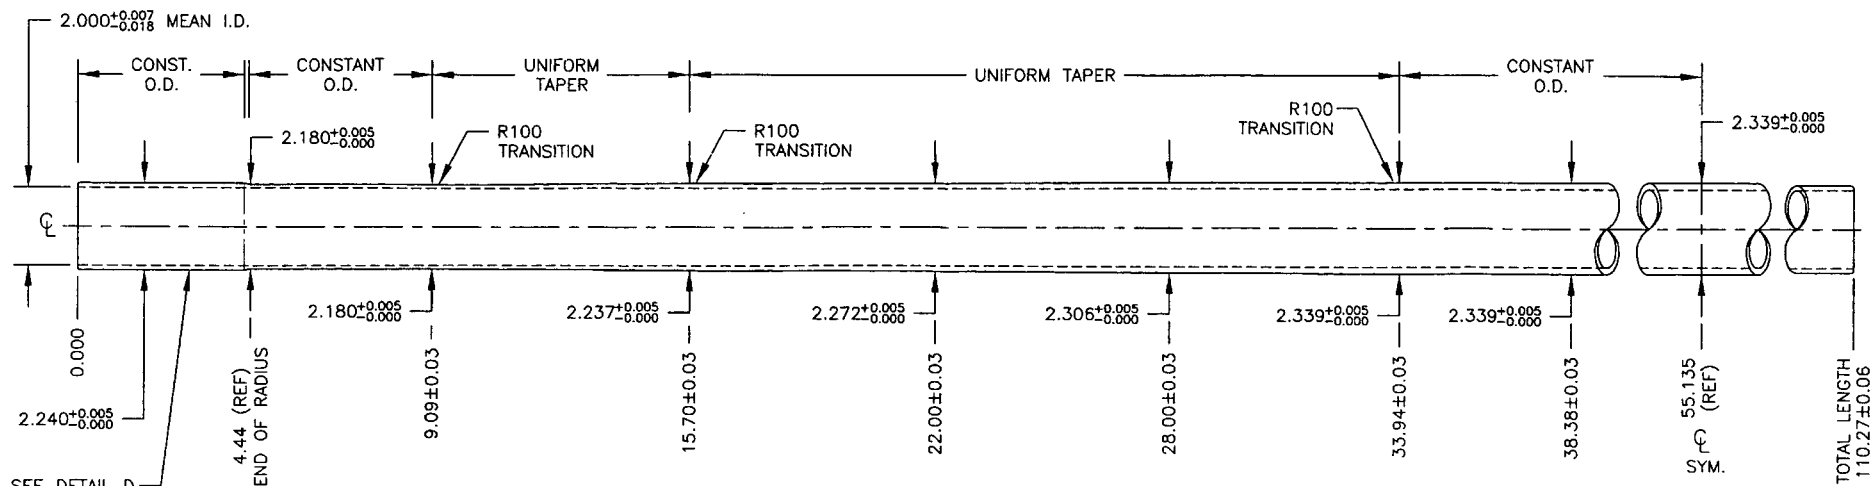

D350-748-141 MACHINING DETAIL

**DETAIL D: CUFF
SCALE 1:1**

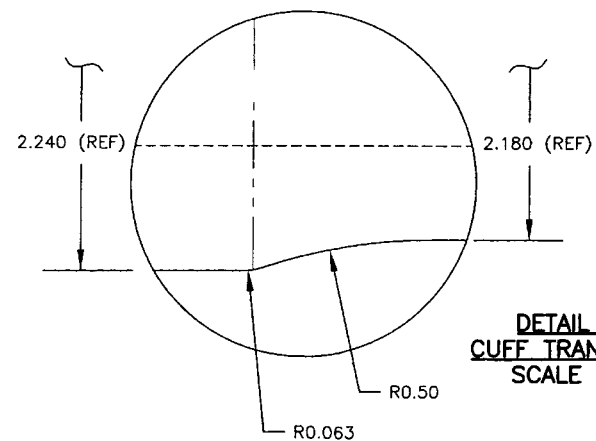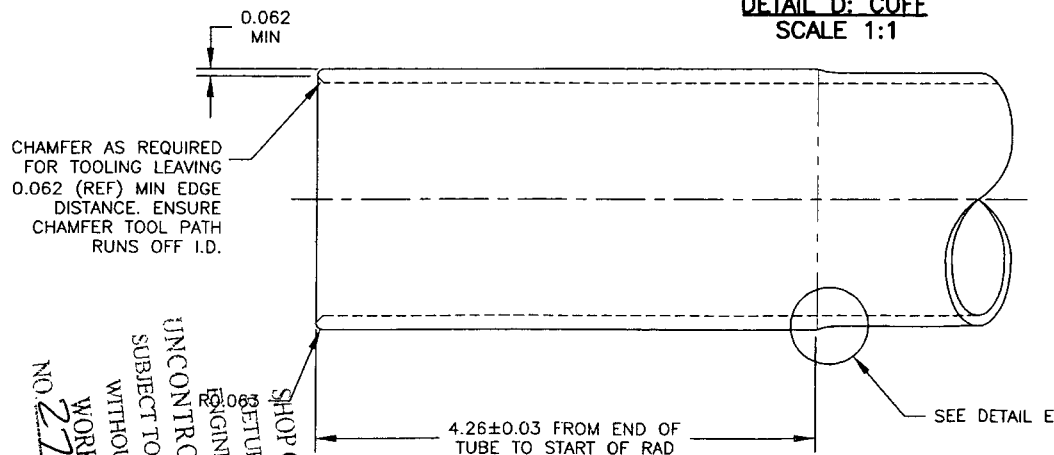

**DETAIL E:
CUFF TRANSITION
SCALE 9:1**

PRELIMINARY DRAWING

UNCONTROLLED COPY
SUBJECT TO AMENDMENT
WITHOUT NOTICE
WORK ORDER
NO 278234

COPYRIGHT © 2006 BY DART AEROSPACE LTD.		DESIGN 9P	DRAWN BY	DART	DART AEROSPACE LTD. WILKESBURY, ONTARIO, CANADA
THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.		CHECKED	APPROVED	DRAWING NO. D350-748-141	REV. B SHEET 3 OF 3
DATE 06.06.30		TITLE CROSSTUBE (AS 350/355 HI FWD)		SCALE 1:3	

DART AEROSPACE LTD		Work Order: 2728 27823A
Description: 35 CROSS TUBE 350 FWD		Part Number: D 350-298-141
Inspection Dwg: b	Rev: B	Page 1 of 1


FIRST ARTICLE INSPECTION CHECKLIST

☒ First Article ☒ Prototype

Drawing Dimension	Tolerance	Actual Dimension	Accept	Reject	Method of Inspection	Comments
0.062	$\pm .010$	0.063	—			
4.26	$\pm .030$	4.278	✓			
2.240	$\pm .005$	2.240	✓			
2.180	$\pm .005$	2.182	✓			
2.180	$\pm .005$	2.184	✓			
2.237	$\pm .005$	2.341	✓			
2.272	$\pm .005$	2.276	✓			
2.306	$\pm .005$	2.310	✓			
2.339	$\pm .005$	2.339	✓			
2.339	$\pm .005$	2.341	✓			
110.27	$\pm .060$	110.27	—			
0.062	$\pm .010$.062	—			
4.26	$\pm .030$	4.26	✓			
2.240	$\pm .005$	2.244	✓			
2.180	$\pm .005$	2.184	✓			
2.180	$\pm .005$	2.184	✓			
2.237	$\pm .005$	2.237	—			
2.272	$\pm .005$	2.274	—			
2.306	$\pm .005$	2.308	✓			
2.339	$\pm .005$	2.339	—			
2.339	$\pm .005$	2.342	✓			

Measured by: TSC	Audited by:	Prototype Approval:
Date: 06	Date:	Date:

Rev	Date	Change	Revised by	Approved
A		New Issue	KJ/JLM	



VAC AERO
INTERNATIONAL INC.

284

PACKING SLIP

OAK 77605-1

07/28/2006

MM / DD / YYYY

PAGE : 1



HEAD OFFICE
1371 SPEERS ROAD, OAKVILLE, ONTARIO
CANADA L6L 2X5
TEL: (905) 827-4171 FAX: (905) 827-7489



QUEBEC DIVISION
7450 RUE VÉRITÉ STREET, ST LAURENT, QUÉBEC
CANADA H4S 1C5
TEL: (514) 334-4240 FAX: (514) 334-6269

GST No. : R105468102

1DAR01

BILL TO: DART AEROSPACE LTD.
1270 ABERDEEN ST.
HAWKESBURY, ON

SHIP TO: DART AEROSPACE LTD.
1270 ABERDEEN ST.
HAWKESBURY, ON

K6A 1K7

K6A 1K7

DATE SHIPPED	SHIP VIA	F.O.B.
07/28/2006		ORIGIN
CUSTOMER P/O No.	JOB No.	TERMS
1709		COD

LN	PART NO	DESCRIPTION	UOM	QTY ORDERED	QTY SHIPPED	B/O QTY
01	D350-CROSS TUBES		EA	8	8	0
		Process Specifications: Procedure: 4353 HEAT TREATED TO 180-200 KSI PER AMS 2759-1C MATERIAL: 4130 D350-748-141 B27823A, B27824A, B27825A, B27826A D350-748-241 B27830A, B27829A, B27827A, B27828A NOTE: SAND BLAST TUBES				
02	LC	LOT CHARGE 320LBS X \$2.26/LB		1	1	0

No claims for shortage in weight or count will be entertained, unless presented within 5 working days after receipt of materials by customer.




VACUUM BRAZING HEAT TREATING SPECIAL PROCESSING FURNACE EQUIPMENT



HEAT

Handwritten signature or initials, possibly "C. J. C." or similar, located in the upper left quadrant of the page.

Handwritten mark or signature, possibly "C. J. C.", located in the lower left quadrant of the page.

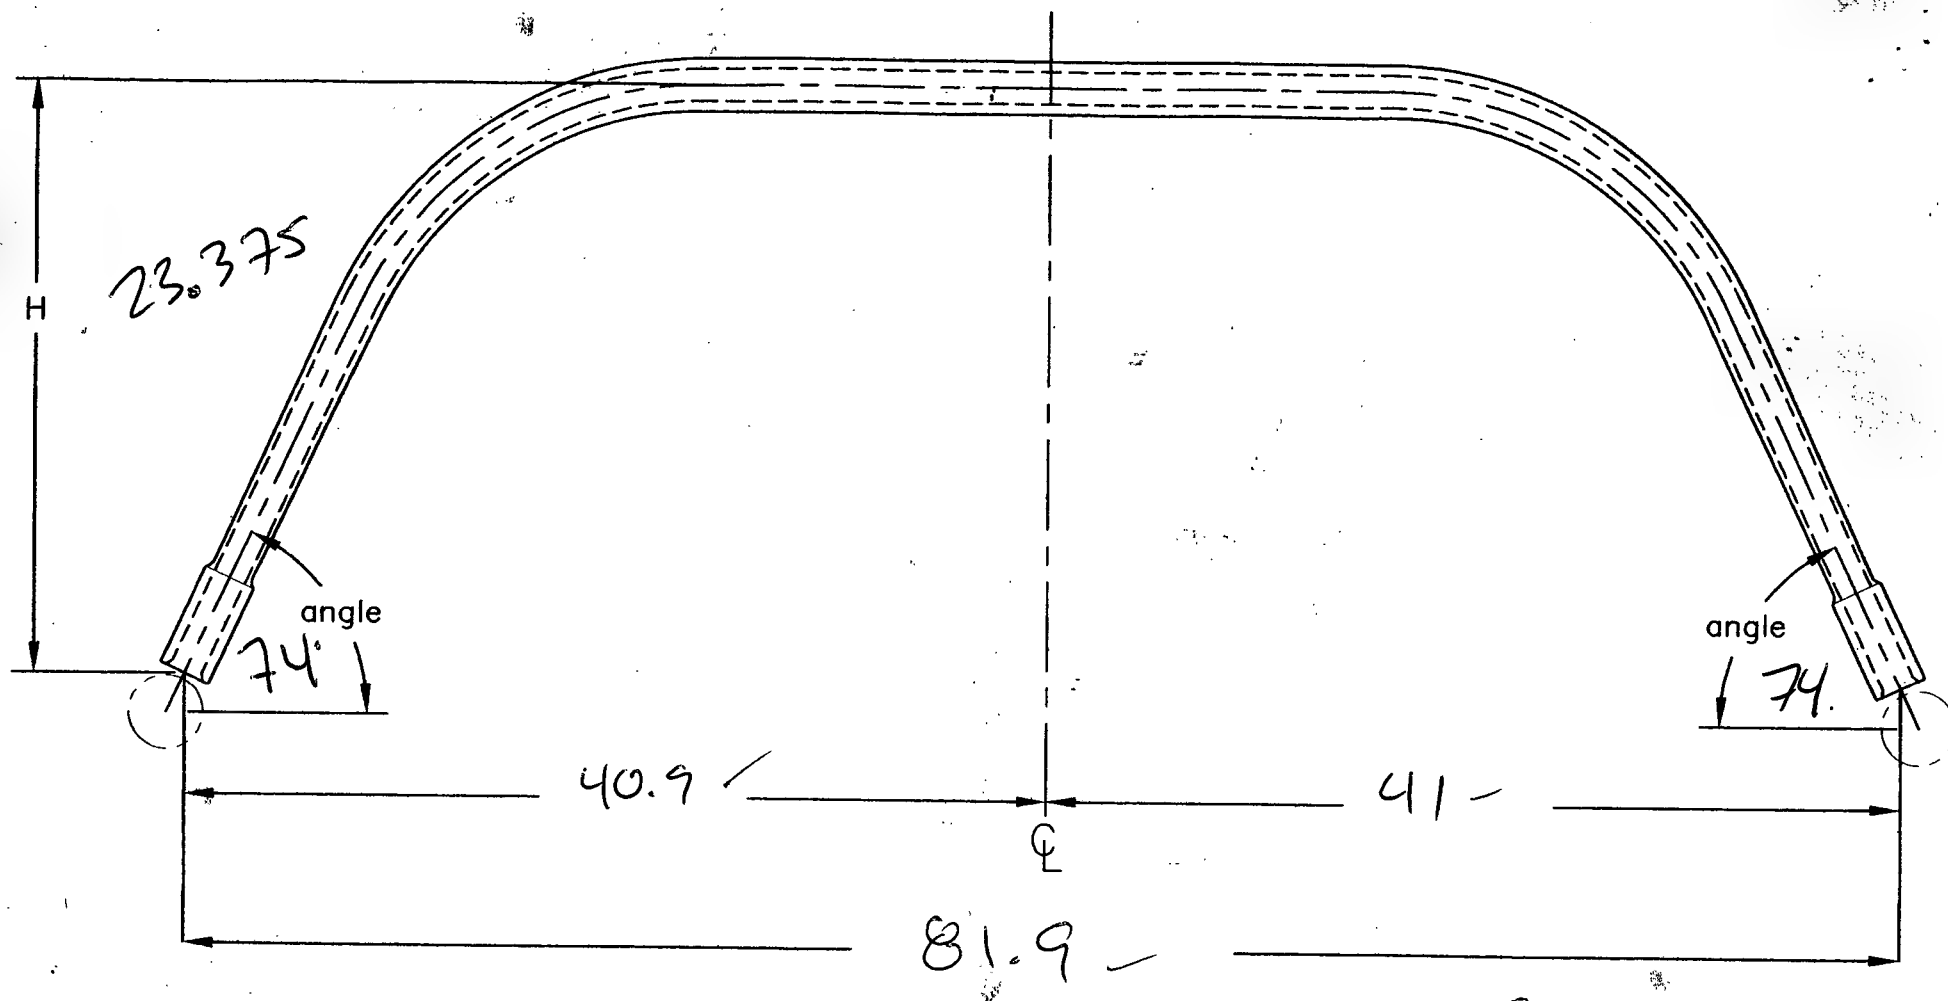

DATE: 06-08-09

DESCRIPTION: 350-748-141

BATCH NO: 27823

DRAWING: 350-Prelim. Rev.B

H: 23.25

1/2 SPAN: 40.9 ±.120

TOTAL SPAN: 81.8 ±.240

ANGLE: 75⁺²₋₀

Boyer
06-09-07



DESIGN <i>qp</i>	DRAWN BY <i>qp</i>	DART AEROSPACE LTD HAWKESBURY, ONTARIO, CANADA	
CHECKED <i>#</i>	APPROVED <i>#</i>	DRAWING NO. D350-748-241	REV. C SHEET 1 OF 3
DATE 06.08.14		TITLE CROSSTUBE (AS 350/355 HI AFT) SCALE NTS	
A	06.03.31	NEW ISSUE	
B	06.06.30	ADD D6018-125 & PRIME AND PAINT	
C	06.08.14	ADD CAD PLATING	

QTY	P/N	DESCRIPTION
X	D350-748-241	CROSSTUBE ASSEMBLY (AS 350/355 HI AFT)
1	D6018-125	CROSSTUBE (OR D6015-125)
2	D3502-1	SUPPORT
2	D2856-400-710	ABRASION STRIP
1	AELS-1032-225	INSERT
1	AN960JD10	WASHER
2	MS21920-20	CLAMP (PER DART SPEC. M-MS21920-20)
1	MS27039-1-10	SCREW

D350-748-141 CROSSTUBE:


- 1) MATERIAL: MANUFACTURED FROM D6018-125 OR D6015-125
FINISHED LENGTH = 122.70±0.06
- 2) MACHINE PER MACHINING DETAIL ON PAGE 3. BLEND OUT ALL EDGES FROM MACHINING LONGITUDINALLY, TRANSITIONS SHOULD BE SMOOTH. NOTE: ALL HOLES ARE DRILLED AFTER BENDING.
- 3) SCRIBE DART PART NUMBER AND BATCH NUMBER IN THIS AREA WITH VIBRATING STYLUS.
- 4) BEND PROGRESSIVELY WITH A MINIMUM OF 7 PASSES. MAXIMUM TUBE FLATTENING DUE TO BENDING IS 6% BASED ON O.D.
- 5) HEAT TREAT TO MIN. 180 KSI PER MIL-T-6736 OR AMS 2759-1C AFTER TURNING
- 6) FINISH: CADMIUM PLATE PER QQ-P-416F, CLASS 1, TYPE II
MAGNETIC PARTICLE INSPECT PER ASTM E1444 AFTER CADMIUM PLATING
PRIME INSIDE AND OUTSIDE PER DART QSI 005 4.2
PAINT OUTSIDE PER DART QSI 005 4.2
- 7) EXTREME CARE MUST BE TAKEN TO PROTECT THE OUTSIDE SURFACE OF THE TUBE. THE OUTSIDE SURFACE MUST BE SMOOTH AND FREE FROM SURFACE DEFECTS SUCH AS SCRATCHES, NICKS, OR DENTS. DEFECTS UP TO 0.005" MAY BE BLENDED OUT LONGITUDINALLY. CIRCUMFERENTIAL GRIND MARKS ARE UNACCEPTABLE. WHEN DRILLING HOLES EXTREME CARE MUST BE TAKEN AND CAREFUL DEBURRING PERFORMED TO ENSURE A CLEAN HOLE WITH NO CRACKING/CHIPPING/GROOVES.
- 8) INSTALL D2856-400-710 ABRASION STRIP WITH A GAP ON BOTTOM SIDE OF CROSSTUBE, CENTERED OPPOSITE D3502-1 SUPPORT, PER QSI 035.
- 9) TORQUE MS21920-20 CLAMPS 60 TO 80 IN-LB
- 10) TOLERANCES ARE PER DART QSI 018 UNLESS OTHERWISE NOTED.
- 11) ALL DIMENSIONS ARE IN INCHES
- 12) PART IS SYMMETRIC ABOUT CENTERLINE EXCEPT FOR Ø0.297 HOLE.

RELEASED

06.08.15 *#*



Copyright © 2006 by DART AEROSPACE LTD

THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.

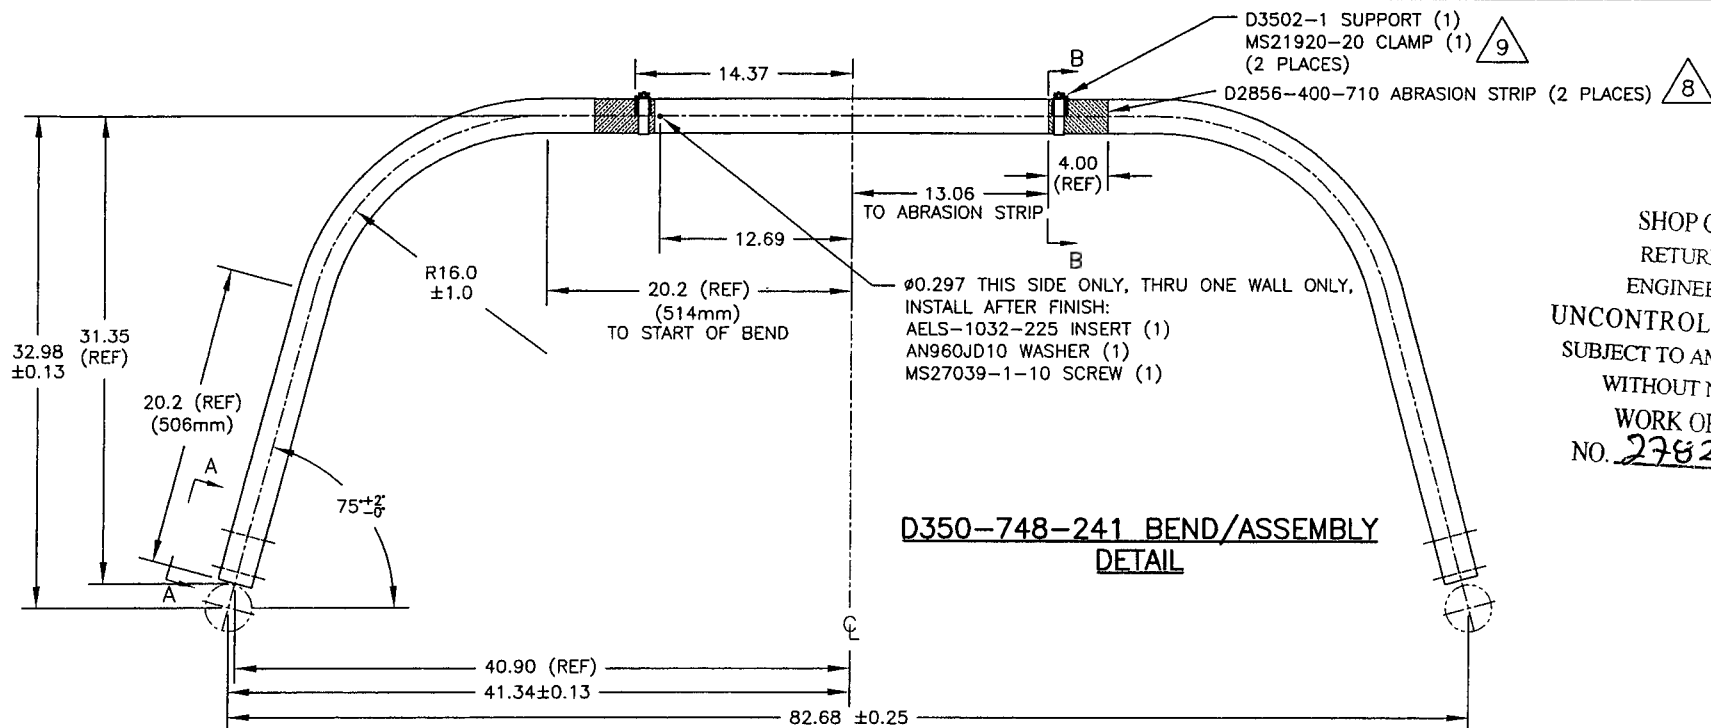

SHOP COPY
RETURN TO
ENGINEERING
UNCONTROLLED COPY
SUBJECT TO AMENDMENT
WITHOUT NOTICE
WORK ORDER
NO. 27823A

D350-748-241 BEND/ASSEMBLY DETAIL

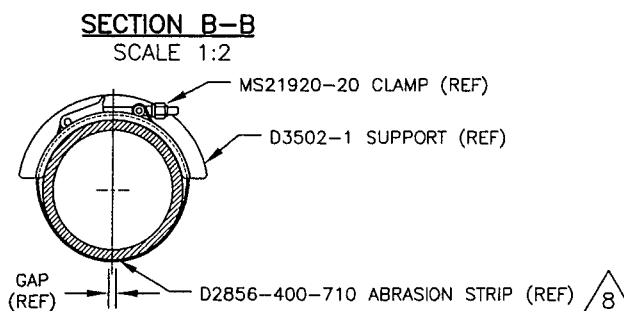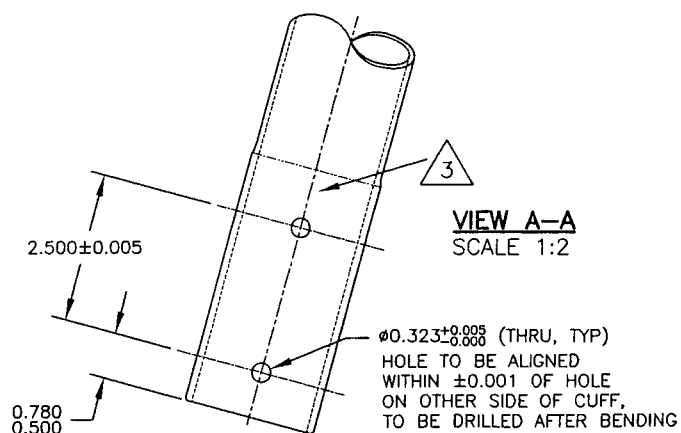

RELEASED
06.08.15

COPYRIGHT © 2008 BY DART AEROSPACE LTD.		DESIGN	q	DRAWN BY	q	DART DART AEROSPACE LTD. HAMMERSBURY, ONTARIO, CANADA	REV. C
THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.		CHECKED	#	APPROVED	#		
DATE		06.08.14		DRAWING NO.		D350-748-241	SHEET 2 OF 3
TITLE		CROSSTUBE (AS 350/355 HI AFT)		SCALE		1:8	

PACKING LIST

PACKING LIST NO: 310991
DATE: 09/22/06

DART AEROSPACE
1270 ABERDEEN STREET
HAWKESBURG ON K6A 1-K7

P.O. NUMBER: 274711

TERMS: C.O.D.

QUANTITY BALANCE PART NUMBER/DESCRIPTION
SHIPPED QTY

1	0	D350-748-141	S/N: B27825A JOB: 542793
1	0	D350-748-141	S/N: B27823A JOB: 542813
1	0	D350-748-141	S/N: B27826A JOB: 542814
1	0	D350-748-241	S/N: B27830A JOB: 542815
1	0	D350-748-241	S/N: B72827A JOB: 542816
1	0	D350-748-241	S/N: B27828A JOB: 542817

1. Stress relieve at 350-400°F for 4 hours minimum
2. Cadmium plate per AMS-QQ-P-416B, Type II, Class 1 (QQ-P-416, Type II, Class 1)
3. Embrittlement relieve within 4 hours of plating at 350-400°F for 8 hours minimum
4. Magnetic particle inspect per ASTM E 1444-05. No linear indications/cracks allowed.

Qty Ins: 6 Qty Rej: 0 Qty Acc: 6

PACKING LIST

PACKING LIST NO: 310991
DATE: 09/22/06

DART AEROSPACE
1270 ABERDEEN STREET
HAWKESBURG ON K6A 1-K7

P.O. NUMBER: 274711

TERMS: C.O.D.

QUANTITY	BALANCE	PART	NUMBER/DESCRIPTION
SHIPPED	QTY		

5. Inspect

Docn No.:
Ship Via: OTHERS

K



SOUTHWEST

United Industries, Inc.

422 S. ST. LOUIS / TULSA, OK 74120
PHONE 918-587-4161 / FAX 918-582-6158
ACCOUNTING FAX 918-585-2952

CERTIFICATION

CERT NO: 310991
DATE: 09/22/06

DART AEROSPACE
1270 ABERDEEN STREET
HAWKESBURG ON K6A 1-K7

P.O. NUMBER: 274711

f/s

QUANTITY PART NUMBER/DESCRIPTION

1	D350-748-141	S/N: B27825A JOB: 542793
1	D350-748-141	S/N: B27823A JOB: 542813
1	D350-748-141	S/N: B27826A JOB: 542814
1	D350-748-241	S/N: B27830A JOB: 542815
1	D350-748-241	S/N: B72827A JOB: 542816
1	D350-748-241	S/N: B27828A JOB: 542817

1. Stress relieve at 350-400°F for 4 hours minimum
2. Cadmium plate per AMS-QQ-P-416B, Type II, Class 1 (QQ-P-416, Type II, Class 1)
3. Embrittlement relieve within 4 hours of plating at 350-400°F for 8 hours minimum
4. Magnetic particle inspect per ASTM E 1444-05. No linear indications/cracks allowed.

Qty Ins: 6 Qty Rej: 0 Qty Acc: 6

5. Inspect

WE CERTIFY THAT THE PARTS LISTED ABOVE HAVE BEEN PROCESSED IN ACCORDANCE WITH THE REQUIREMENTS AND SPECIFICATIONS OF THE ABOVE REFERENCED PURCHASE ORDER. DOCUMENTATION IS ON FILE AND AVAILABLE FOR REVIEW



Certification

FAA Repair Station CN2R748K

Randy Bruner
Inspector

NOTE: SUBJECT TO SOUTHWEST COMPANIES, INC. STANDARD TERMS & CONDITIONS

INVOICE

DART AEROSPACE
1270 ABERDEEN STREET
HAWKESBURG ON K6A 1-K7

INVOICE NO: 310991
DATE: 09/22/06
SHIP DATE: 09/22/06
P.O. NUMBER: 274711
TERMS: C.O.D.

QUANTITY	PART NUMBER/DESCRIPTION	UNIT PRICE	AMOUNT
1	D350-748-141 S/N: B27825A JOB: 542793	1980.00	1980.00
1	D350-748-141 S/N: B27823A JOB: 542813		
1	D350-748-141 S/N: B27826A JOB: 542814		
1	D350-748-241 S/N: B27830A JOB: 542815		
1	D350-748-241 S/N: B72827A JOB: 542816		
1	D350-748-241 S/N: B27828A JOB: 542817		

1. Stress relieve at 350-400°F for 4 hours minimum
2. Cadmium plate per AMS-QQ-P-416B, Type II, Class 1 (QQ-P-416, Type II, Class 1)
3. Embrittlement relieve within 4 hours of plating at 350-400°F for 8 hours minimum
4. Magnetic particle inspect per ASTM E 1444-05. No linear indications/cracks allowed.

Qty Ins: 6 Qty Rej: 0 Qty Acc: 6

INVOICE

DART AEROSPACE
1270 ABERDEEN STREET
HAWKESBURG ON K6A 1-K7

INVOICE NO: 310991
DATE: 09/22/06
SHIP DATE: 09/22/06
P.O. NUMBER: 274711
TERMS: C.O.D.

QUANTITY PART NUMBER/DESCRIPTION

UNIT PRICE AMOUNT

5. Inspect

Docn No.:
Ship Via: OTHERS

K

Total Amount -----
1980.00

Chris Provencal

From: David Shepherd [dshepherd@dartaero.com]
Sent: October 3, 2006 10:03 AM
To: 'Chris Provencal'
Cc: 'S Shahbazian'; 'Beckett, Bill'
Subject: RE: 350 xtube cad plating

Chris,

I think the modified CAD plating procedure is acceptable.

As we discussed, I had some concern about the stress relieving comment on the packing slip because I didn't realize that by heating up the tubes, we would be stress relieving them. We didn't test our crosstubes in a stress relieved condition. The crosstubes we tested had compressive stresses in the tensile stress areas of the crosstube. However, because the highest stress areas are in the unbent portion of the crosstube and because I think we had so much margin in our drop test (no shock absorbers, damaged parts, overloaded, etc ...), my gut tells me that we are OK and I don't think we need to re-test.

I'm glad to hear that we are dimensionally checking the crosstubes after all the heating. I think this step should be added to the work order on receiving inspection for every crosstube.

As we discussed, I think a drawing revision is in order. I think reference to a QSI for the procedure outlined on the packing slip would be best.

David

From: Chris Provencal [mailto:cprovencal@dartaero.com]
Sent: Monday, October 02, 2006 2:17 PM
To: David Shepherd (David Shepherd)
Cc: 'S Shahbazian'; 'Bill Beckett (Bill Beckett)'
Subject: 350 xtube cad plating

David,

There is another set of 350 xtubes they want to send out tomorrow. I don't know if you've had a chance to review the cad plating issue. They're eager to get a response.

To recap:

-I originally told you that the magnetic particle was done first. That was the plan, but they ended up following the drawing (cad->magnetic). The invoice I sent you gives the correct order the work was done.

-The cad plating was done to AMS-QQ-P-416B (issued 2004 by SAE) instead of the drawing's' QQ-P-416F (issued 1991 by military). I don't see a problem with this since it's a more current issue, and the only reason specified QQ-P-416F is because that's what the "old" never-used supplier suggested.

-The dims were re-checked after cad plating and the dimensions did not change.

-An NCR has been created to address the problem with the work orders. The bigger issue is that one was sent to a customer and we need to take action on that one asap.

If you need more info, let me know.

03/10/2006

